

INCIDENT STATUS SUMMARY

1. **Incident Name** – HOTEL RELEASE
2. **Operational Period** – 04/23/21 – 04/29/21
3. **Type of Incident** – OIL SPILL
4. **Situation Summary as of the time of the report:**

The NAVY contracted PENCO via the USCG BOA to take over the on water response, recover product, identify areas in which the leak is presenting, and isolate those areas to prevent migration, and investigate/search for the source via excavations.

PENCO continues to maintain a very effective booming strategy, adjusting and replacing sorbents/boom as needed. Hotel1 corner all the way to the Halawa stream end of (b) (3) (A) is boomed, contained, and strategically isolated prevent migration. The effectiveness of the booming strategy continues to be effective in preventing product and sheen from escaping the boomed areas. Ocean boom will be installed a tertiary containment layer. The dilapidated fence section was repaired on 4/28, and measuring for the tide riser was completed.

The excavating that began on 3/2 continues very deliberately and cautiously. The same tools are still being used being used for digging include a backhoe, an air spade, water jet, hand shovel, posthole diggers and a vactor truck to vacuum the soil and small rocks. Spoils and debris are being carefully monitored and collected in predesignated areas.

The Defuel line *remains* the suspected source of the light fuel. – 4/29

-All active fuel lines have been tested and passed, both pressure testing and (b) (4) precision leak testing.

-Defuel line failed both tests

-The Defuel line has six 1" thermal expansion lines that connect to it from the active system

-In late January blank flanges (skillets) were placed in the defuel line to ensure it was isolated.

-From early March through 9 April light colored (apparently fresh) fuel that was being recovered from K111 and trench #4. No light colored fuel has been seen since.

- The amount of dark colored oil being recovered from within the VS3 fence line since 9 April has been very small

- -RAA plumes from historical UST/fuel encompasses the site

5. Future Outlook/Goals/Needs/Issues:

-Continue interdiction, containment and recovery efforts

-Continue looking into the remaining abandoned lines as a possible source

PRESENT COA (Prep began 4/23)

- Remove and recover the legacy oil and any active oil release in the vicinity of VS-3 using natural and induced flow of the oil & ground water to intercepting trenches.

PENCO will use induced and natural ground water flow, recycled through topside oil/water separators, to recover and remove the subsurface oil. Ground water will carry the subsurface oil to downslope (East to West), to the intercepting trenches (#3). Pumps will recover water and oil from the intercepting trench 3, through oil water separators, and reintroduce the water in the upslope wells, in the vicinity of the restroom. The groundwater assisted by the reintroduced water will push the oil to the downslope trenches, where it will be pumped, put through the oil water separator and again reintroduced. The cycle will continue as needed to clean the area of oil and prevent it from going into the water

-The Eastern edge of the plume has been located on the West edge of the restroom lawn.

-This is the upstream/hill area where we want to reintroduce the water.

- PENCO will dig a 5w x 17L trench (for 4 x 16 shoring)

- HGS' vactor rig is down, but should be fully operational on Monday.

There is no evidence of a current leak from one of the active lines at VS-3. All oil recently recovered has been medium to dark in color.

Our Goals:

1. On-water containment and recovery.

-No sheens observed escaping containment

-We have seen an increase in oil. Mostly believed to be caused by the current lunar cycle which has caused some recent higher and lower tides).

2. Prevent oil from reaching the water by intercepting it on land.

-Continuing to intercept on land. We have seen the oil mostly disappear from within the VS3 fence line

3. Locate the source

-As of 4/29 it is theorized that the defuel line was a source that may have slowly leaked for a period of time before the release was discovered. The release was enhanced by the recent line testing that required not only the Defuel line to be packed with fuel, but all of the other lines that have the aforementioned 1" thermal expansion lines feeding into the defuel line. The darkened oil is from the microbial actions that take place. Once the Defuel line was isolated with the skillets, the light colored fuel tapered off and stopped.


-We believe that there may be additional contributing sources such as the RAA1 plume and spills from site history.

-Abandoned line tapping began today with the 6" PVC waste oil line in both trenches 2 and 8. 3/8" holes drained the line of water in trench 2. The line was empty in trench. The holes are being repaired and the pipe is being capped. Trenches 2, 8, 9 have been filled in.

-Trench 4 has been above the active lines has been completely filled in to spec. (gravel, geo textile, non-contaminated soil)

-The casing was tapped in trench 3. Two 3/8" holes. The casing drained water for approximately 30 minutes followed by several minutes of fuel that tapered off and stopped. 34

gallons of dark fuel, similar in appearance to the majority of oil being recovered on site. The holes were plugged and will be reopened on Monday for evaluation.

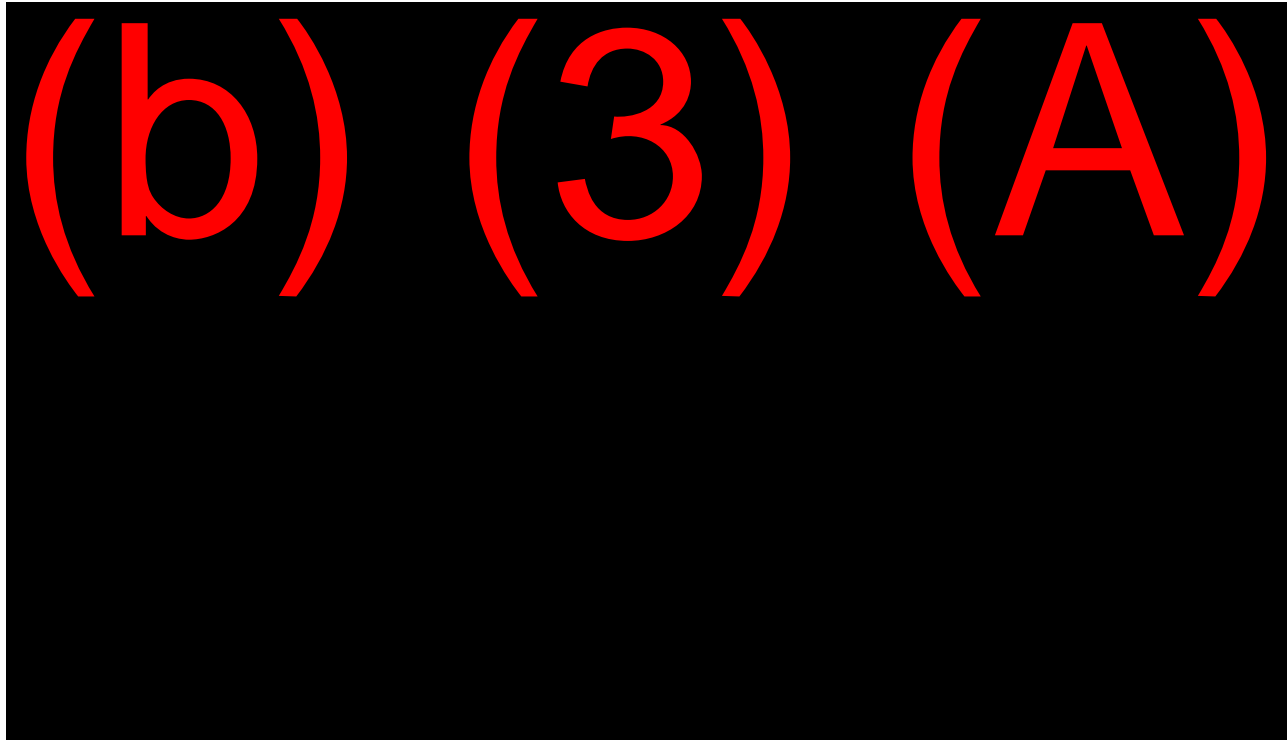

Dig diagram as of 4/28

6. Safety Status/Personnel Casualty Summary: No injuries. No Deaths.

- a. VOCs at ground level at the excavations continue to read 0-2ppms. Spikes of ~10ppm are seen near the floor of the excavations. 4/22 - 19 VOC PPMs in trench 3. Personnel working in trenches have proper protection.
- b. MultiRAE meters are being used on site at all times when digging is in progress or product is being recovered from the K111 vault or the excavations.
- c. Personnel who may eventually work in the trenches will wear respiratory protection.
- d. Grounding cables are being used for the skimmer operations in the K111 and will also be used in trench #4 due to the discovery of an abandoned concrete electrical conduit.
 - i. Current dig plan will fill back in the area of the electrical conduit
- e. All required safety measures for digging deeper than four feet will be strictly adhered to.
- f. There are several safety concerns with digging that will be addressed prior to placing personnel in excavations:
 - i. 10 plus feet deep
 - ii. Working below ground water
 - iii. Type C soil
 - iv. Working in fuel
 - v. Working/digging on and around active lines
 - vi. Excavating areas that have been previously excavate.
- g. We have determined our soil to be type C. Type C is the most unstable and therefore the most dangerous.

- h. Potholing is helping minimize the number of large excavations and thereby minimizing digging hazards.
- i. Each day begins with an onsite safety brief. Safety is paramount.

7. **Property Damage:** NONE

8. **Attachments:** NONE

9. **Equipment Resources in use/on site**

PENCO EQUIPMENT ONSITE

- a. 1 x 17 ft Boston Whaler
- b. 1400 ft harbor boom
- c. 3 x Berms
- d. 36 x Steel plates for covering excavations
- e. Drums 55 gal as required
- f. 1 x Reach lift/JLG
- g. 1 x Conex box for drum storage
- h. 1 x Backhoe
- i. 1 x 6,430 gal IMO (FRAC tank)
- j. 1 x air compressor
- k. 1 x Vacuum truck
- m. 1 x brush skimmers
- n. 1,000 ft ocean boom
- o. Decanting tank (oil/water separator)
- p. HPU for brush skimmer
- q. Vactor truck-off-site from 4/27 for repair
- r. 1 x Conex box for emergency response gear
- s. Shoring boxes and shoring material/system

10. **Personnel Resources working full time on Hotel Release:**

- a. NAVY – 1 NOSC REP (FOSC)
- b. CONTRACTOR-Varies with different operations 5-17 onsite on any given day
 - i. 1 PM
 - ii. 2 Equipment Operators
 - iii. 1 Foreman
 - iv. 2 Divers
 - v. 1 Dive Master
 - vi. 2 Dive tenders
 - vii. 2 Drivers
 - viii. 5 Technicians
 - ix. 2 x Air excavating crew (vactor operators)

**Divers have not been needed in recent weeks, but may be called in as needed.*

11. **RECOVERED PRODUCT ESTIMATES:**

- a. **Recovered 4/23– 4/29/21 = 362**

- b. Total recovered by the JBPHH Facility Response Team (FRT) from 3/17/20 until 2/11/21 = 3100 gallons
- c. Total Recovered by BOA contractor, PENCO from 2/12/21 – 4/29/21 = 3481 gallons
- d. Total since 3/17/20 = **6581**.

12. Waste

- a. 187 Drums total drums removed by PENCO and transferred to Clean Energy
- b. 4681 total gallons (4,293 water and 388 oil) was removed via trailered IMO by PENCO for disposal. 4/14.

PREPARED BY:

Derrell Saul, Navy On-Scene Coordinator Rep (NOSC)
